




Report VTC 16th of December 2013

- 1 Storage Room
- 2 Kitchen and Restaurant
- 3 Classroom 1
- 4 Classroom 2
- 5 Classroom 3
- 6 Classroom 4
- 7 Sanitary Girls
- 8 Boarding Girls 1
- 9 Boarding Girls 2
- 10 Computerroom
- 11 Library 1
- 12 Library 2
- 13 Administration 1
- 14 Administration 2
- 15 Administration 3
- 16 Sanitary Boys
- 17 Boarding Boys 1
- 18 Boarding Boys 2
- 19 Practical 1
- 20 Practical 2
- 21 Practical 3
- 22 Practical 4
- 23 Practical 5
- 24 Carpentry Workshop
- 25 Auto mechanics Workshop
- 26 Auditorium
- 27 Classroom 5
- 28 Classroom 6
- 29 Classroom 7
- 30 Classroom 8
- 31 Teachers Houses
- 32 Piggery
- 33 Poultry
- 34 Laboratory & Waterbassin
- 35 Cattle shed

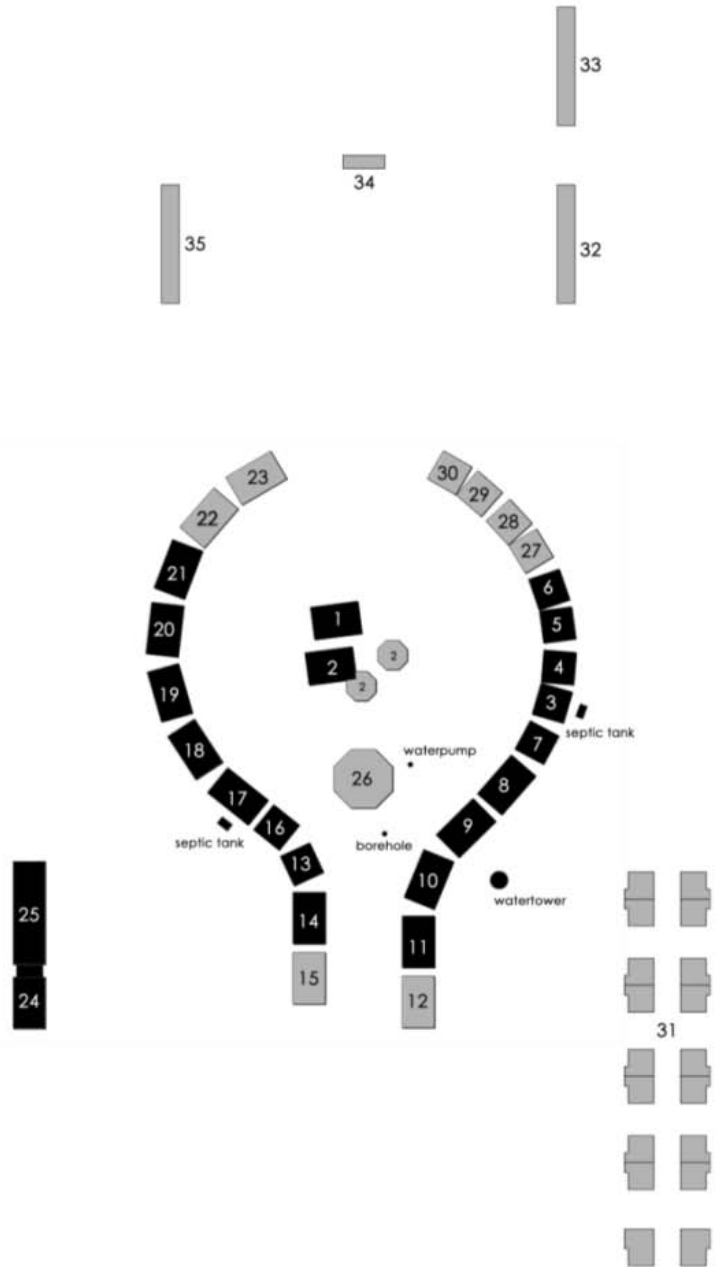

- Phase 1
- Phase 2



Girls Wing – December 2013

Dear members GKMT,

Following you'll find the monthly report on the activities at the VTC.

1 Storage Room (Temporary carpentry workshop). We have installed the extraction system, 2 table saws, woodmilling machine, planing machine, drilling machine, sanding machine, radial saw and the compressor. Each machine has been connected as shown by members from the Zwolle group, meaning that every machine is supplied with its own break switch and also a main switch is installed. The mentioned machines are all in use (↓).



8 Boarding Girls 1. Assembled and fixed four interior doors on the left side (↑). Except for painting and ceilings this building is finished.

9 Boarding Gilrs 2. Finished thatching the roof(↓), assembled and fixed all the window frames, finished the window sills, finished covering and finished plastering the interior walls(↓).



11 Library 1. Assembled and fixed all the window frames (↓).



13 Administration 1. Finished covering, cross ventilation, assembled and fixed window frames(↑).

14 Administration 2. Finished covering backside, assembled and fixed all window frames(↓).



16 Sanitary Boys. Assembled and fixed window frames(↓).



17 Boarding Boys 1. Finished interior masonry up to ring beam level including reinforcement of the foundation(↑).

18 Boarding boys 2. Finished the foundation box(↓).



Veranda. On the girl's wing, on the front side of the veranda we finished the gutter except for filling it with crushed stones(↑). At the back we finished digging and putting PVC and deformed bars(↓).




Other. During two weeks we could not use the truck while it was in the workshop for serious repair. This caused the lacking of materials, in particular cement. Carpentry could continue without problems but a group of helpers had to work on activities that were not planned. The remaining of an anthill at the middle of the plot has been dug away in order to level the field(↑).


Plotnumber. The Ministry of Land in Ndola has assigned us plotnumber: 39750. Unfortunately this does not mark the end of the procedure to confirm our plot. The coordinates in the drawing from the planning office show that our plot is twice as big as assumed until now. It appears that in the past GCMF bought two pieces of land within our own plot from neighboring families (Kafweni and Milambo). In order to fix this situation I'll do a proposal to the both families to trade the needlessly acquired pieces of land for pieces of the same size outside of the plot. Ones agreed on by the two families and witnessed by the director of works of the council, I'll have to go back to the Planning Office and the Ministry of Land with the new coordinates. All this has to be done before I can apply for the building permit. See drawing on next page.

PLOT NR. 39750, Mpongwe


Drawn by Planning Office

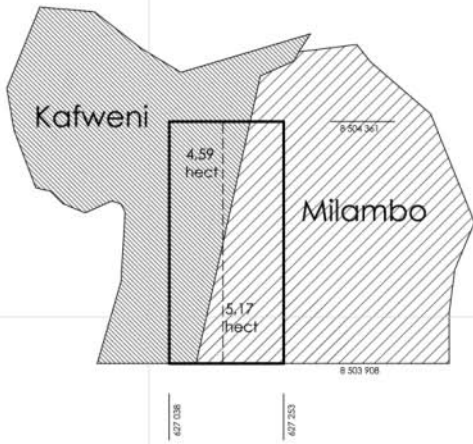


Old contracts show this as our plot

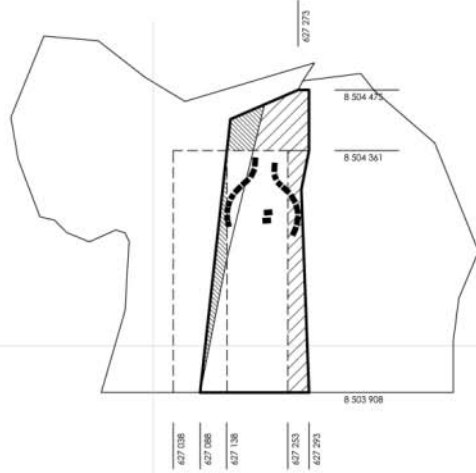


Bought from Kafweni

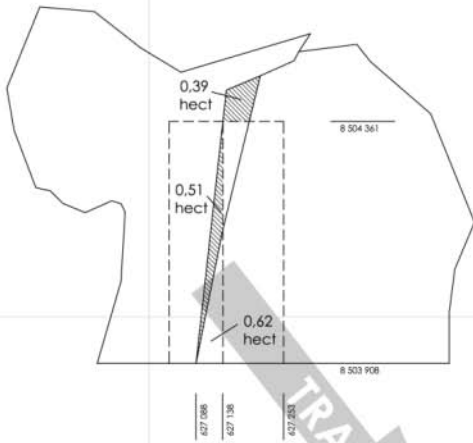

Bought from Milambo

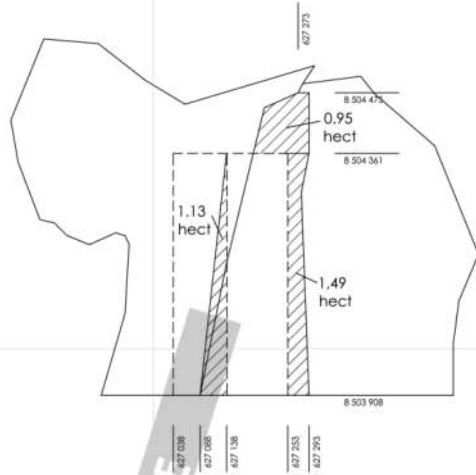

Desired by GCMF

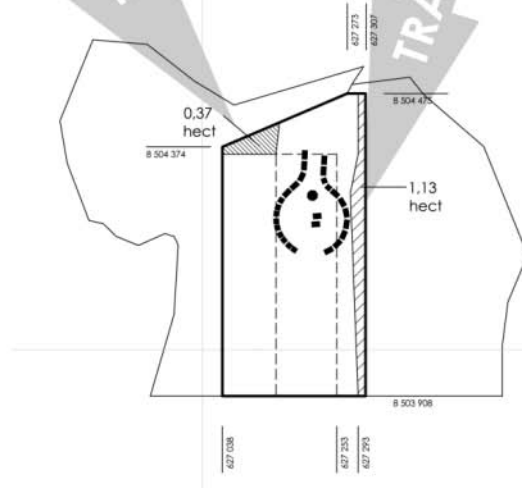

Kind regards, Bram

